

Work Products Workflow

Merjola Prifti
Senior Associate | Project Management

Contacts for Work Products management:

Merjola Prifti
Senior Associate | Project Management

PMO-Trading
SharedMailbox

These workflows descriptions are aimed for Project Management Officer (PMO), for Work Product Owners (WPO), For-Review-Only role (FRO) & For-Signature-Only role in Alfresco (FSO).
Templates: Group Project Portfolio Management - Project Management Templates - All Documents (sharepoint.com)
Other related content added, as of 8th Sep, 2025:
Mandatory Manual Labeling of Office Documents as of September 13
Classification and Labelling

TO WPO:

Notify PMO upon starting with a WP creation

Each Work Product goes in several rounds of the workflows (Internal Review, L1 Review, L1 Sign Off, Final), all being tracked within the WP Matrix → *planned dates*. When the WP Owner/Author starts with a specific Work Product, PMO team must be informed via email, so the WP Matrix is updated with the '*Actual dates*'.

- **When the WP Owner (WPO) starts with the document, an informing email should go to PMO team** - *PMO-Trading@deutsche-boerse.com* – otherwise you will be reminded when the due date is passed, and the name is shown in the WP-To-Focus list.
- Alternatively, if the WPO forgets to inform PMO when creating the WP, **WPO *should* inform PMO, when the document is sent for Internal Review** (PMO in CC). PMO can then update the 'WP Creation → Actual Date' column H.

DO NOT finish/start any workflow in Alfresco yourself

- The WP Owners shall *only* respond to the comments made in Alfresco, Set the priority & the status of response (*„No Action"*, *„Accepted comment"* or *„Future Consideration*). Choosing one of the three options, would then allow PMO to finish the Handle Review.
- The PMO should finish/start any workflow In Alfresco (L1 review/L1 Sign Off) in Alfresco, not WP Owners.

Reminder on ZIP File Naming and Structure when using versioning


Please note, when following the structure for ZIP files, it's important to correctly rename the main ZIP file as described below. The file names within the ZIP can be shortened or use abbreviations where appropriate, because it may be challenging to unzip them for the Reviewers, due to the length of many characters:

- Remove redundant parts such as **"T7 release 14.0"** from ZIP file names.



- Use abbreviations where possible (e.g., **"Version 1"** → **"V1"**).
- Consider **shortening the title of your WPID**, if it helps reduce the overall file name length and let PMO update the WP Matrix title too, to have consistency.

- Example would be a combination of all

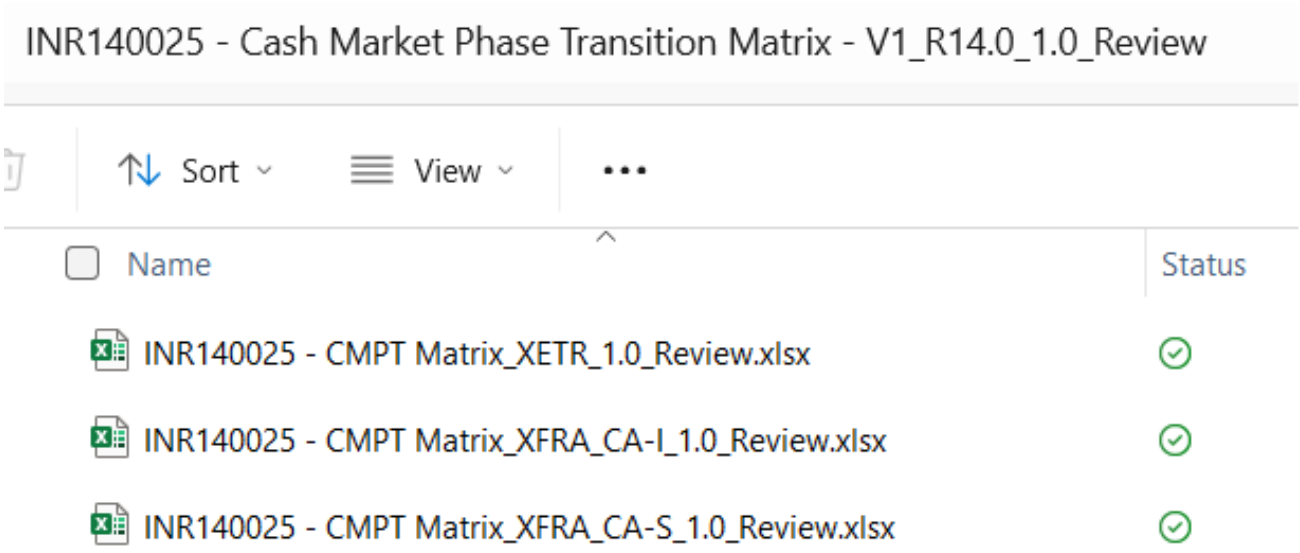


Remove 'printed' row date field in WP cover page

It is *recommended* to remove the outdated 'printed' date field on the cover page of the work documents. It does not seem to fit the times anymore.



Title field (WP Matrix & Alfresco)

- **Document titles within the WP Matrix & Alfresco** → it is not allowed to have a title with commas (,) semicolon (;) -→ Instead, put a dash (-) ; underscore (_), or space ( ).



Work Product Management Versioning Process:

Before checking this, please note this disclaimer for the zip files here

1. Initial Document Stages: Draft and Internal Review

- **Versioning:** Use version numbers from **0.1 to 0.9**.
- **Format:** WPID - Title_ReleaseNR_Version_Status
- **Example:** PPI131025 – Summit Approach_R13.1_0.1_InternalReview

2. Review Cycle

- **Starting Version:** The Review must begin with version **1.0**.
- **Format:** WPID - Title_ReleaseNR_Version_Status
- **Example:** PPI131025 – Summit Approach_R13.1_1.0_Review
- **Exception:**
  - If a document returns to Review after reaching Sign-Off, continue using the most recent version number. Versions from **1.1 to 1.9** can be used as the document progresses through the review cycle.
  - The version should include the suffix "Review" to indicate its status.
    - Example: PPI131025 – Summit Approach_R13.1_1.5_Review (if the document is reviewed multiple times).

3. L1 Sign-Off Process

- **Starting Version:** The Sign-Off process should begin with version **1.1**.
- **Subsequent Versions:** Continue using the numbering from **1.1 to 1.9** as needed.
- **Format:** WPID - Title_ReleaseNR_Version_Status
- **Example:** PPI131025 – Summit Approach_R13.1_1.1_Sign-Off
- **Exception:**
  - If no changes were made since with the document since last Release, the document can be sent for Sign-Off as version **1.0**.
  - The version should include the suffix "_Sign-Off" to indicate its status.
    - **Example:** PPI131025 – Summit Approach_R13.1_1.0_Sign-Off

4. Final Document Versioning

- **Final Version:** The final version of the document should be labeled as **2.0**.
- **Format:** WPID - Title_ReleaseNR_Version_Status
- **Example:** PPI131025 – Summit Approach_R13.1_2.0_Final
- **Exception:**
  - For W0 type: Final version can be **1.0**.
    - **Example**: SDM131001 - Software Delivery Completion Report_R13.1_**1.0**_Final
  - **Minor Updates:** If changes are minor (e.g., typo correction), silently replace the final document without changing the version number. (in accordance with the WPO)
    - **Example:** PPI131025 – Summit Approach_R13.1_2.0_Final
  - **Significant Updates:** If the changes are substantial, increment the version number accordingly.
    - **Example:** PPI131025 – Summit Approach_R13.1_2.1_Final

General Guidelines

- **Compliance:** WPOs and PMOs must follow the versioning guidelines, including any exceptions, to ensure consistency. These rules apply to all WP types W1. (Note: Do not use W2 due to technical issues with Alfresco.)
- **Important: This applies from 16th September 2024** to projects T7 Major releases (i.e., R13.0, R13.1) and P7 – Eurex Theo Pricing System. It's *crucial* that the review, sign-off process, and final versions are accurate (as they are being tracked in Alfresco as well).
- **Optional Suffix:** Adding the letter 'v' before or after the version number is optional.

- **Public Documents**: Please note, these guidelines refer to internal versioning when saving a document and preparing to initiate workflows or store it in Alfresco. The headers within public documents remain unchanged! Any updates are reflected only when the document is saved—***behind the title***. For example, see below when the WPO sends the review version to PMO to initiate a workflow in Alfresco.
  (Note that the title itself includes "Version 1" and we keep that—this is separate from **Alfresco's internal versioning**.)
  - **Starting Version:** The Review must begin with version **1.0**.
  - **Format:** WPID - Title_**ReleaseNR_Version_Status**
    - **Example:** MMR130X032 – T7 Release 13.0 - Cash Functional/Technical Release Notes (Preliminary) - Version 1_**R13.0_1.0_Review**

  The final version of public documents will be provided to the Product Delivery team (by PMO/WPO) with the title tracked in the WP Matrix.

TO FRO/FSO/PMO

Anticipating Delays & Expediting Review/Sign off Workflow:

Please ensure to follow these procedures to maintain the workflow and avoid any unnecessary WP delays.

Expected Delays (e.g., Out of Office, Planned Holidays):

- **Action:** Reviewers and Signatories must identify their deputies and inform the PMO before their absence.
- **Impact:** These changes will be updated in Alfresco and reflected in the WP Matrix data.

Unexpected Delays (e.g., Unplanned Leave):

- **Action:** If we receive an out-of-office notice without a designated deputy, the PMO will contact the Line Manager to arrange a substitute for the

stakeholder to review/sign the specific WP.

- **Note:** A solid and agreed project plan is one fundament a successful project relies on. The PM Team aims to avoid delegating tasks within Alfresco whenever possible. In individual cases, the review of the absent person can be canceled, and the new deputy will be assigned. (*Note: This is up to PMO, after alignment with Business and IT PM*.)

General Guidance:

- **To PMO: If in doubt:** Always discuss the necessary actions directly with the PM Team during the Tuesday WP2Focus meeting.
- **Ongoing Delays:** If the delay continues, the PMO will address this during the WP2Focus meeting to determine if it is necessary to arrange review/sign-off closing meetings.
- **Implicit Review/Sign-off (see also here Work Products Workflow):** If stakeholders do not attend the closing meeting and complete their review/sign-off on time, the PMO will consider it as an implicit review/sign-off.

TO PMOs:

Finish L1 Review Workflow in case:

When each of the reviewers has clicked on the '*Finish Review*' option:

1. If the finished reviews are done without comments in Alfresco. -> the PMO would finish the L1 Review Workflow in Alfresco, notify the Owner about it, and request the Sign off version at the same time.
2. If the finished reviews are done with comments which need the Owner responses. –> PMO would ask the WP Owner to do so in Alfresco. When this task is completed from the WPO, PMO would finish the L1 Review Workflow in Alfresco, notify the Owner about it, and request the Sign off version at the same time.
3. If the finished reviews are done with comments, and the Owner has provided the responses. –> PMO would finish the L1 Review Workflow in Alfresco, notify the Owner about it, and request the Sign off version at the same time.

Note 1: Regardless of when the Sign off version reaches PMO inbox - *it may come even several days later* – we do close the L1 Review workflow, to keep the timeline tied and keep things moving.

Note 2: Only these statuses are allowed in Alfresco: "No Action", "Accepted comment" or "Future Consideration". Others, would throw an error message and will not allow PMO to finish the L1 Review workflow.

Note 3: Once the L1 review is completed (finished), it is no longer possible to reactivate the L1 Handle review. If we open the L1 Review workflow, the WP will still go in another round of an open Review for the rest of the Reviewers too and we do not want to do that (if their review and comments were provided once already).

Schedule Closing meetings (L1 Review/L1 Sign Off)

- When WPs are overdue, the list is brought to PM (D. Tescan) & HoD (U. Meyer) attention on 'WP-To-Focus' meeting, every Tuesday.
- *Only* with the request of D. Tescan & U. Meyer, closing meetings can be organised by the PMO. Other similar requests sent from others to us are *not* mandatory, however in free capacity, PMO *can help* organise such meetings on *ad-hock* basis.
- Such meetings shall be organised by the PMO shared calendar, but i*t can happen to be organised by the personal calendar of the PMO as wel*l. Requesting 'mandatory presence' of the *affected* reviewers/signatories that are overdue & WP Owner. The PM/PMO members, *they* can be added as *optional participants*.
- The WP Owners may freely organise such meetings on their end too, in case there are WP overdue in Alfresco, with the respective Reviewers/Signatories.



Note for PMO:
To schedule meeting with Manfred Matusza, it's advised to check the calendar with Cintia Petermann (her substitute is Nicole Staude).
To schedule meeting with Dmitrij Senko, it's advised to check the calendar with Georgine Sarbinowski (or email to MaGi@eurex.com) - her substitute is Margareth Nazar, and both have one shared mailbox.

Filling dates for different WP Types (W0 vs W1)

Within the WP Matrix, there are two Work Product Types, WO and W1. When filling the dates, there are some differences, as outlined below:

- **Type WO** – Without L1 Review and Sign Off cycle in Alfresco – simply store in Alfresco and Finish status immediately.
  - Within the WP matrix for **WO Types, skip the Level 1** (L1 - Review & L1 - Sign Off), by leaving the green field dates empty. Macro will work without dates there.

- **Type W1** – With complete L1 Review & Sign Off & Final included.
  - Within the WP matrix for **W1 Types, all the Planned dates should be filled**.
  - Exceptional cases: when L1 Review can be skipped (agreed with WP Owner/PM). Then, the Actual date in 'M' can be equal to Readiness for L1 Review 'J'. Filling the 'M' means that this is the date when the Sign Off workflow started in Alfresco.
  - When L1 review is skipped (PMO did not start a workflow in Alfresco) → then it is recommended to add an actual date in the green field (not a

dummy one) within the WP Matrix.
    - Dummy dates (*1900-01-01)* can be added after the name of the individual reviewer, to inform that a particular person has only FRO/FSO role)

Calculating dates of a WP workflow timeline:

Calculations of days are recommended to start from (Monday to Friday). Exceptions can be adjusted manually. (*Possibly excluding weekends, CZ&DE known public holidays, such as Christmas, Eastern, etc*).

- **WP Creation**: From *Plan Start* (column **G** in WPM) → *Plan Readiness for L1 Review* (columns **I** in WPM) - **4 weeks** for the completion of the document (including work of WPO & Internal review)
- **L1 Review**: From *Plan Readiness for L1 Review* (column **I** in WPM) → *Plan L1 Review end* (columns **L** in WPM) - **5 business days** for the completion of the document.
- **L1 Sign-Off**: From *Plan L1 Review end* (column **L** in WPM) → *Plan L1 Sign Off end* (columns **N** in WPM) - **3 business days** for the completion of the document.
- **Final Delivery:** From *Plan L1 Sign Off end* (column **N** in WPM) → *Plan Final delivery* (columns **P** in WPM) - **same day as L1 Sign Off.**
